Hanover St Garage Restoration

Mon 4/8/24
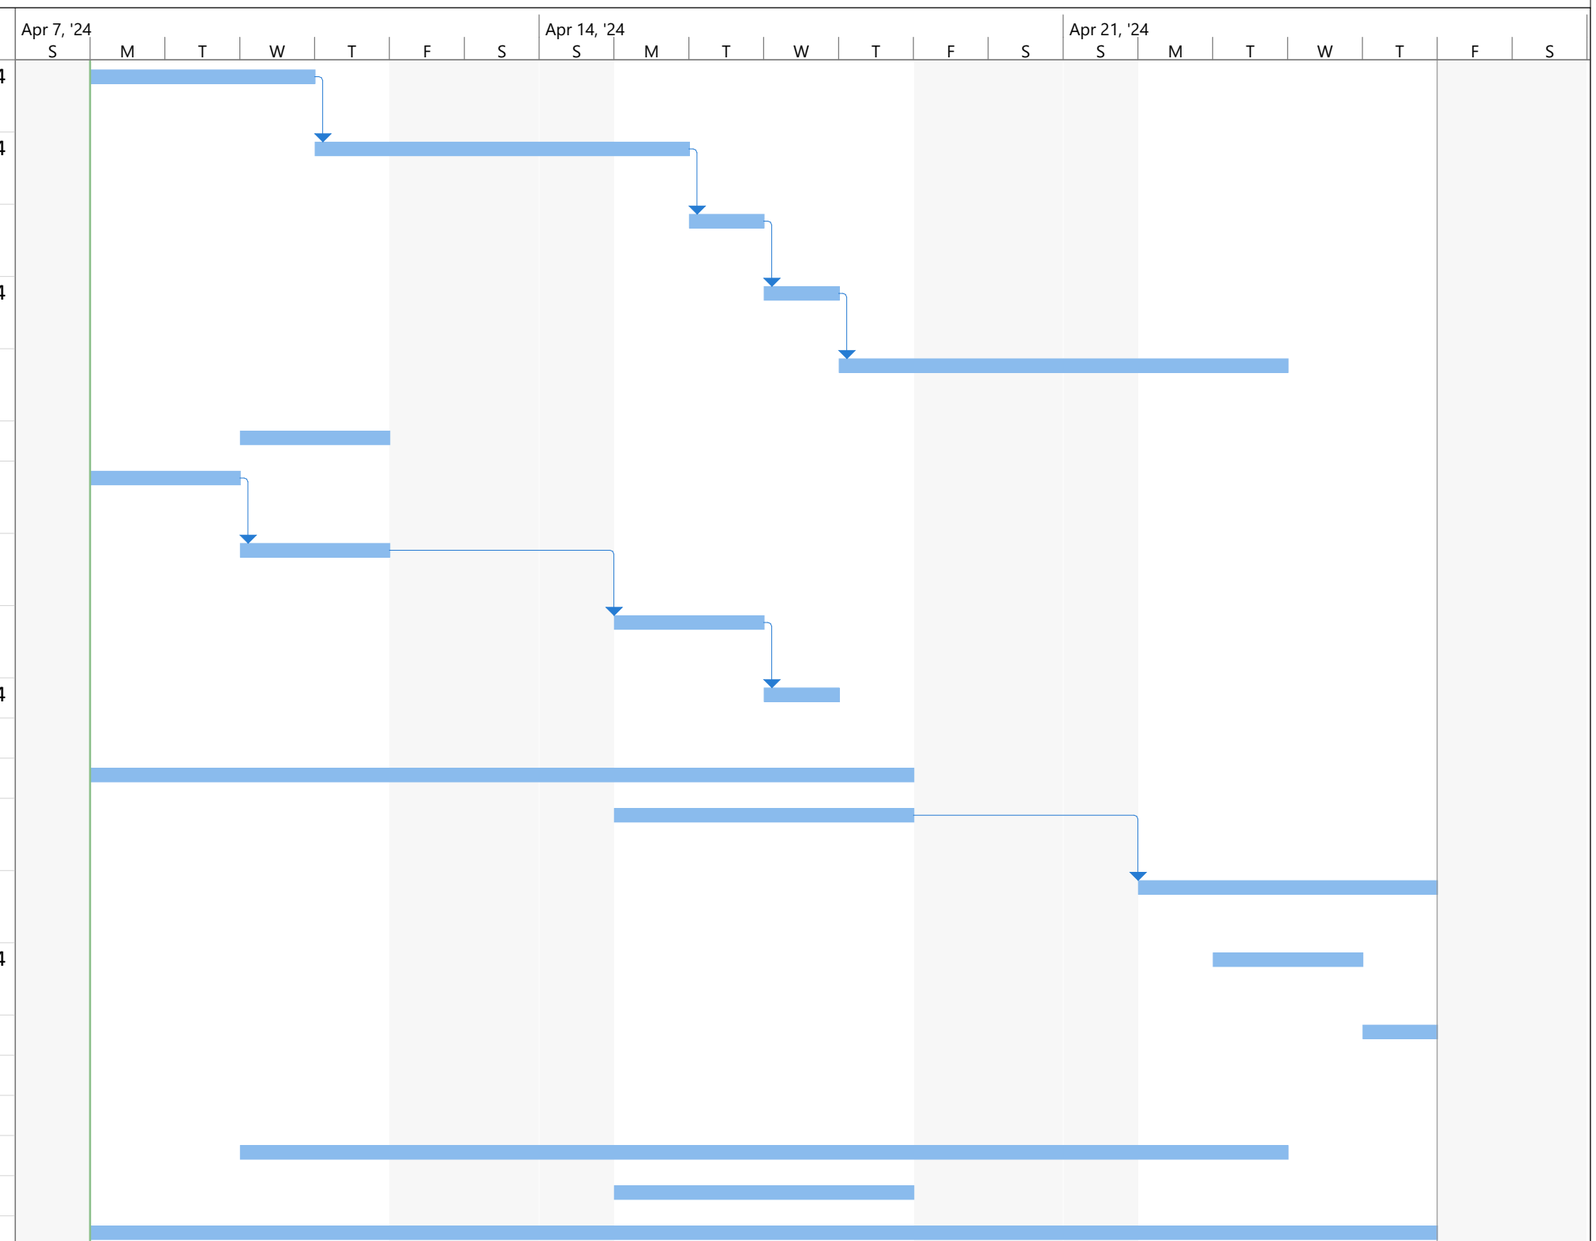
ID	Task Name	Duration	Start	Finish
1	Concrete Curing Period - Level 3 Column 16/17	3 days	Mon 4/8/24	Wed 4/10/24
2	Entrance Concrete Repairs - Level 2 Column 16/17 - Demo (W.I. 3.1, 3.3, 3.6)	2 days	Thu 4/11/24	Mon 4/15/24
3	Entrance Concrete Repairs - Level 2 Column 16/17 - Rebar/Prep (W.I. 3.1, 3.3, 3.6)	1 day	Tue 4/16/24	Tue 4/16/24
4	Entrance Concrete Repairs - Level 2 Column 16/17 - Pour/Clean (W.I. 3.1, 3.3, 3.6)	1 day	Wed 4/17/24	Wed 4/17/24
5	Concrete Curing Period - Level 2 Column 16/17	3 days	Thu 4/18/24	Tue 4/23/24
6	Ladd St Stair Tower Scaling Repairs (W.I. 3.	2 days	Wed 4/10/24	Thu 4/11/24
7	Column Repair - Level 1 - Shoring (W.I. 6.6, 6.7)	2 days	Mon 4/8/24	Tue 4/9/24
8	Column Repair - Level 1 - Demo (W.I. 6.6, 6.7)	2 days	Wed 4/10/24	Thu 4/11/24
9	Column Repair - Level 1 - Rebar (W.I. 6.6, 6.7)	2 days	Mon 4/15/24	Tue 4/16/24
10	Column Repair - Level 1 - Pour (W.I. 6.6, 6.	1 day	Wed 4/17/24	Wed 4/17/24
12				
13	Hanover St Entrance Curb Reconfiguration	8 days	Mon 4/8/24	Thu 4/18/24
14	Install New Steel Lintel Beam/Opening - High St Stair Tower - Level 2 (W.I. 46.3)	4 days	Mon 4/15/24	Thu 4/18/24
15	Install New Ramp/Curb at Elevator/Stair Tower - Level 2	4 days	Mon 4/22/24	Thu 4/25/24
16	Install New Bollards and Delineators (W.I. 43.4, 43.5)	2 days	Tue 4/23/24	Wed 4/24/24
17	New Crosswalk Striping (W.I. 45.5)	1 day	Thu 4/25/24	Thu 4/25/24
18				
19	Subcontractor Work			
20	Landscaping Subcontractor	8 days	Wed 4/10/24	Tue 4/23/24
21	Fencing Subcontractor	4 days	Mon 4/15/24	Thu 4/18/24
11	Painting Subcontractor	12 days	Mon 4/8/24	Thu 4/25/24
